



Siddheshwar Temple

*Great
Indian
Bustard*



Copyright Raja Furchit, Pune



© Joanna Van Gruisen / ARDEA LONDON

UIDSSMT

REMODELING

TRANSMISSION AND


DISTREBUTION SYSTEM

ABOUT SOLAPUR

- ❑ DISTRICT HEADQUARTER
- ❑ 'D'CLASS MUNICIPAL CORPORATION
- ❑ ESTABLISHED IN THE YEAR 1964
- ❑ AREA- 178.57 SQ.KM
- ❑ POPULATION -8.72 LACS
- ❑ TRANSPORT HUB. NH-9,13,211
PASS THROUGH IT
- ❑ BG RAILWAY LINE CONNECTS
SOLAPUR TO BOMBAY
- ❑ FAMOUS FOR TEXTILES AND A
PILGRIM HUB
- ❑ GOOD EDUCATION AND MEDICAL
FASCILITIES





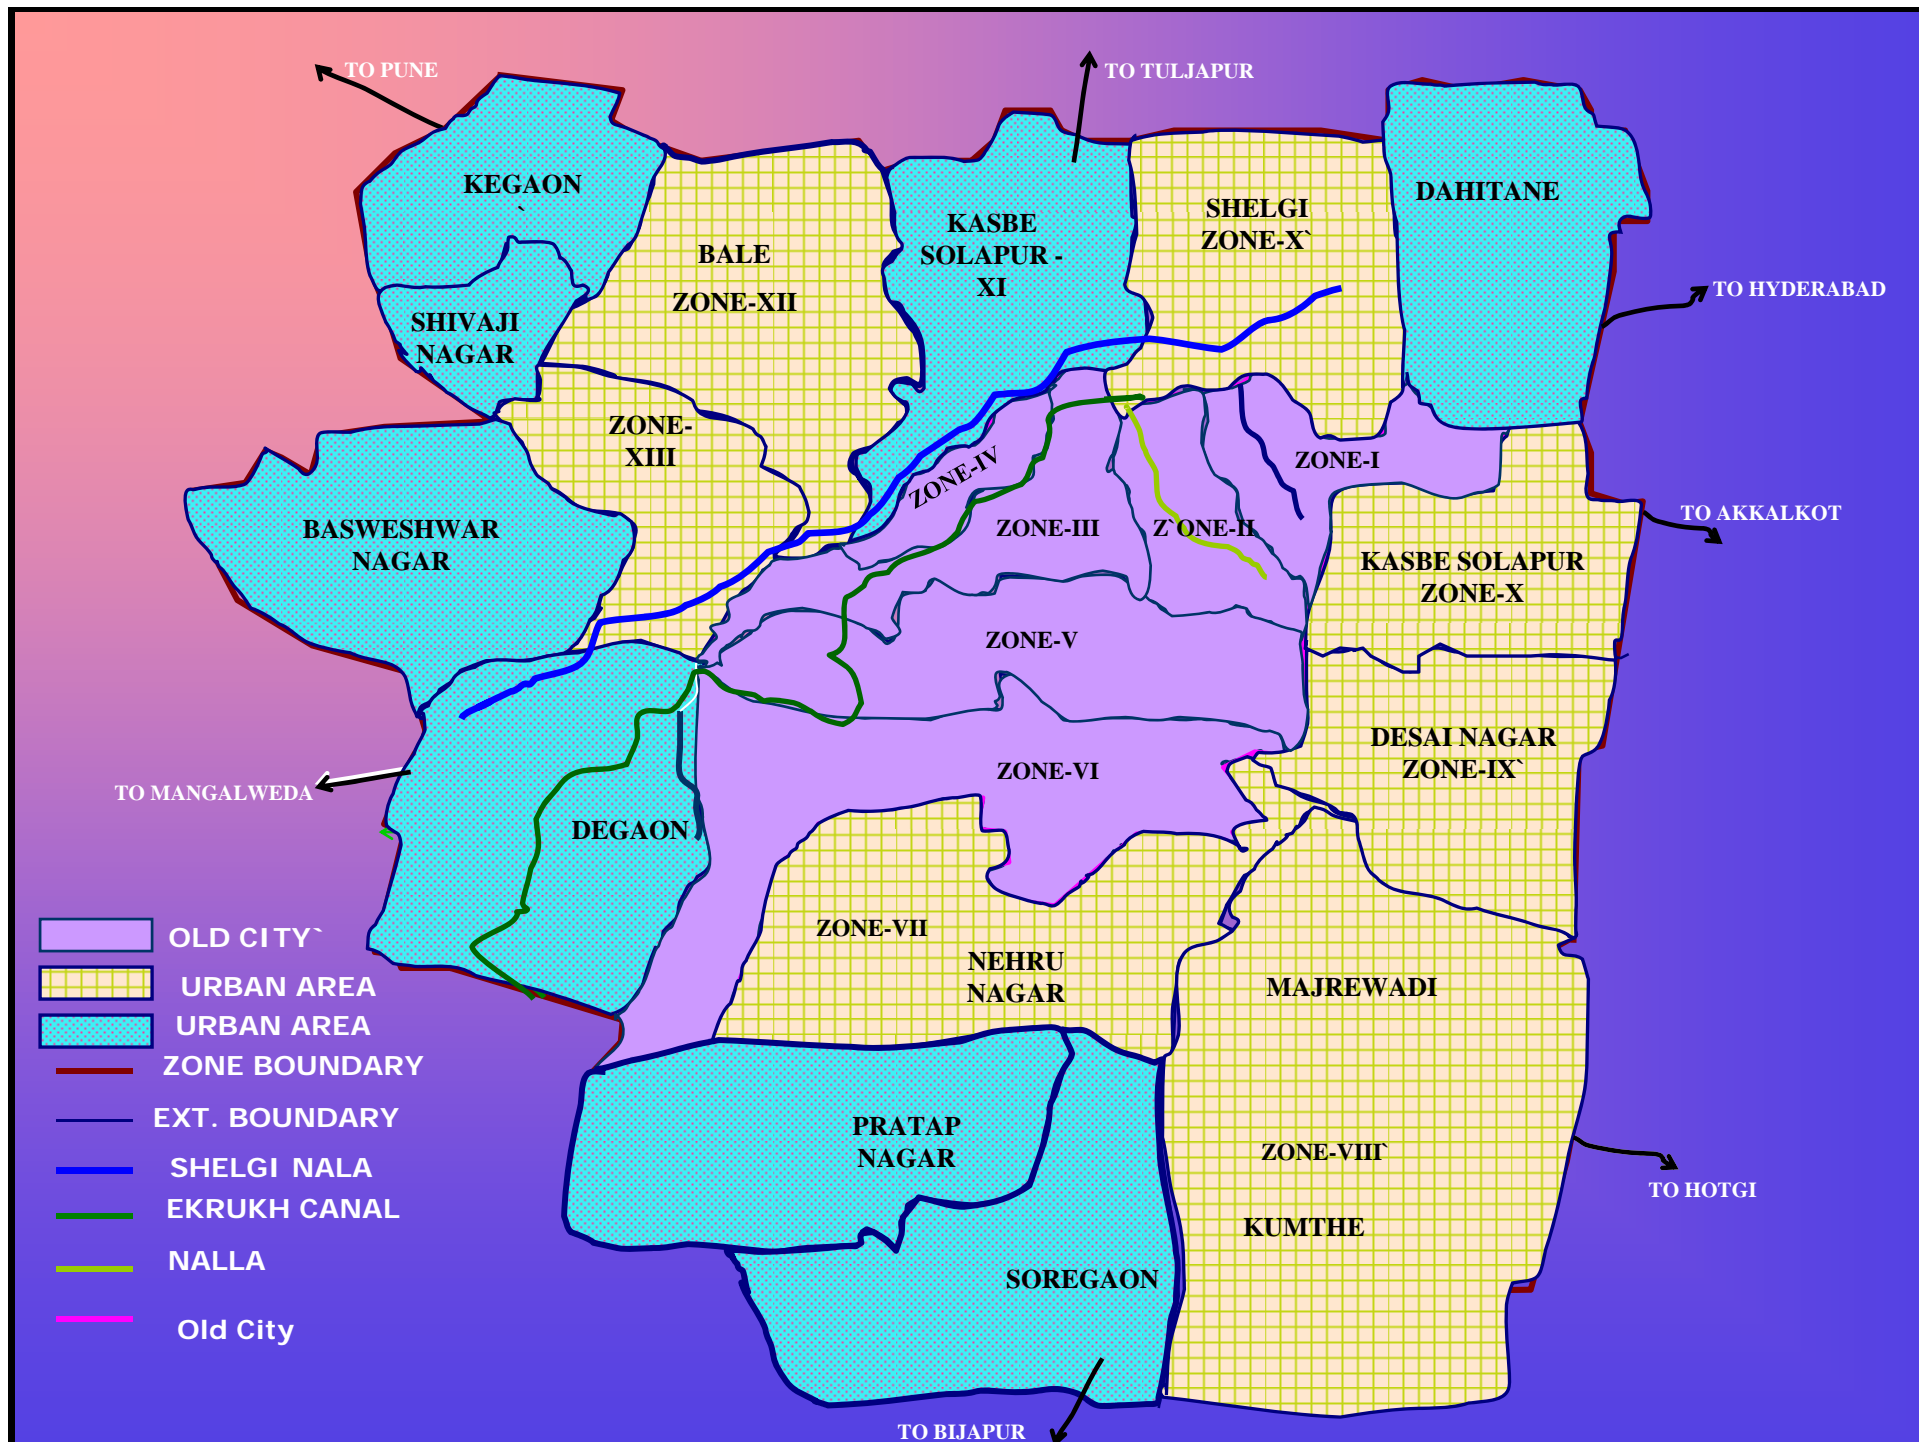

FINANCIAL PATTERN

(Rs in crores)

Sr No		Financial Pattern		Receipt of I st Installment		Receipt of II nd Installment	
1	Central Governm ent	80%	57.6 0	May 2009	28.79	July 2012	28.79
2	State Governm ent	10%	7.20	Supt 2010	3.59	July 2012	3.59
3	Solapur Municipal Corporati on	10%	7.20		7.89		
		Total	72.0 0	Total	40.27	Total	32.38

SUBWORK AND COST

Sr. No.	Name of sub-work	Quantity	Cost as per appraisal of SLNA (Rs Crores)	Expenditure	Present Position
1	Transmission Pipe Line	42.00 KM	20.43	14.43	Work is in progress 30 KM Completed
2	ESR's	17 Nos	10.88	10.13	10 ESR's completed 2 ESR's 90% Completed 2 ESR's 70% Completed 1 ESR's 20% Completed 2 ESR's not Started as Land aq. Process not completed
3	Distribution Pipe Line	171 KM	40.67	40.53	Work is in progress 74 KM Completed
			71.98	65.09	

Expected Date of completion of Project
March 2014

Thank You

